




MAP SHOWING THE ONGOING PROJECTS IN CN/SWR

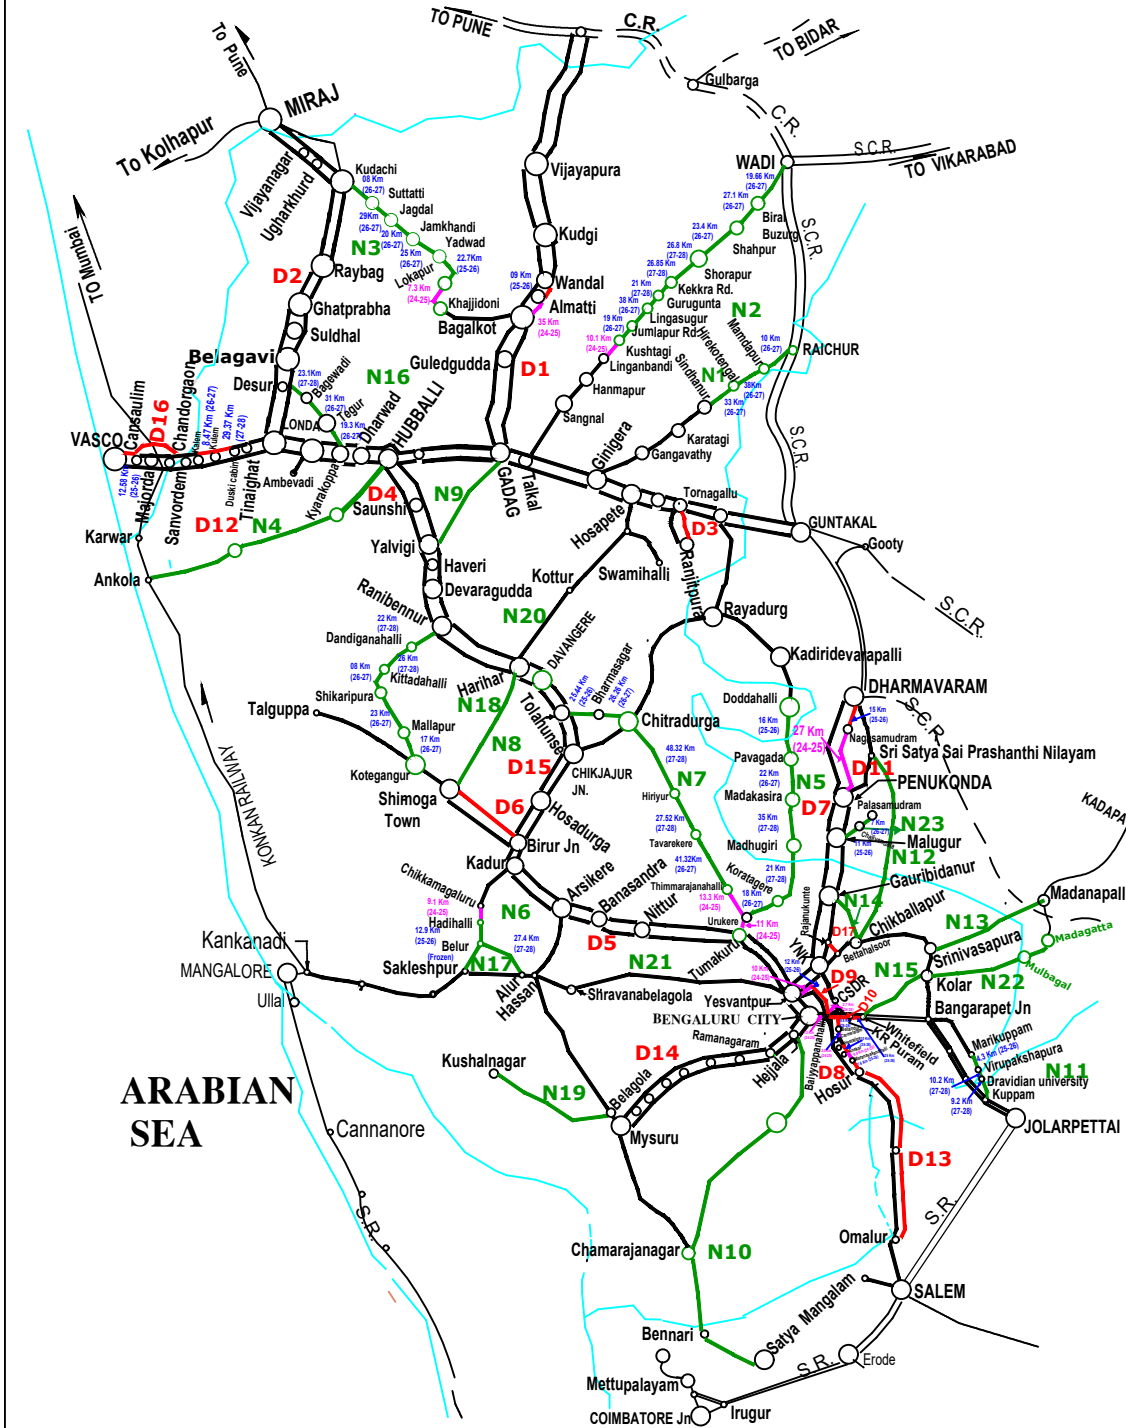

LEGEND

1	DOUBLING (COMMISSIONED)	
2	DOUBLING (BALANCE)	
3	NEW LINE (COMMISSIONED)	
4	NEW LINE (BALANCE)	
5	EXISTING	
6	STATE BOUNDARY	
7	TARGET 2024-25	
8	SECTION BEYOND 2024-25	

NEW LINES

Sl. No	Name of the project	Length in Km.	Comp. Length in Km.	Bal. Length in Km.	Sanct./Amt. cost in Cr.	Agency/ CE in charge	Remarks/TDC
N1	Ginigera - Raichur	165	84	81	3401.22	CE/II/UBL	Mar-2027
N2	Gadag-Wadi	257	46	211	2842	CE/II/UBL	Mar-2028
N3	Bagalkot - Kudachi	142	30	112	1649.31	CE/II/UBL	Mar-2027
N4	Hubballi - Ankola	164	-	164	5174	CE/II/UBL	Under review as per directions of NBWL
N5	Tumukur - Rayadurga	206	83	123	2495.58	CE/II/BNC	Feb-2028
N6	Kadur - Chikmagalur - Belur	68	46	22	825.30	CE/II/BNC	Dec-2025
N7	Tumukur - Chitradurga Davangere	182	-	182	1801	CE/II/BNC	Dec-2027
N8	Shimoga - Harihar	79	-	79	832	CE/II/BNC	No LA by GoK
N9	Gadag - Yalvigi	58	-	58	675	CE/II/UBL	DPR under prep.
N10	Bengaluru - Satyamangalam (260 km) Part - Hejajla Chamarajanagar	142	-	142	1383	CE/II/BNC	RB decision awaited
N11	Marikuppam - Kuppam	24	-	24	297	CE/II/BNC	Dec-2027
N12	Chikkaballapur - Puttaparthi - Sri Satya Sai Prashanthi Nilayam	103	-	103	692	CE/II/BNC	CCEA Clearance awaited
N13	Srinivasapuram - Madanapalli	75	-	75	467	CE/II/BNC	FLS under progress
N14	Chikkaballapur - Gauribidanur	44	-	44	368	CE/II/BNC	FLS under progress
N15	Whitefield - Kolar	53	-	53	349	CE/II/BNC	No LA by GoK
N16	Belvige - Dharwad	73	-	73	927	CE/II/UBL	Dec-2027
N17	Hassan - Belur	27	-	27	749	CE/II/BNC	Dec-2027
N18	Shimoga - Shikaripura - Ranibennur	96	-	96	994.47	CE/II/BNC	Dec-2027
N19	Mysuru - Kushalnagar	87	-	87	1855	CE/II/BNC	DPR under process for sanction
N20	Kottur - Harihar	65	65	-	489	CE/II/UBL	Commissioned on 03.03.2014
N21	Hassan - Bengaluru via Shravanabelgola	166	166	-	1763	CE/II/BNC	Commissioned on 26.03.2017
N22	Kolar - Mulbagal - Madagatta	51	-	51	783	CE/II/BNC	No work from SCR end
N23	Malugur - Palasamudram	18	-	18	342.14	CE/II/BNC	Dec-2026
TOTAL		2345	520	1826	31,154		

DOUBLING

Sl. No	Name of the project	Length in Km.	Comp. Length in Km.	Bal. Length in Km.	Sanct./Anti cost in Cr.	Agency/ CE in charge	TDC/Remarks
D1	Hotgi - Kudgi - Gadag	284	240	44	2460	CE/II/UBL	Feb-2026
D2	Londa - Miraj	186	186	-	1591	CE/II/UBL	Commissioned on 19.01.2024
D3	Tornagallu - Ranjipura	23	-	23	147	CE/II/UBL	DPR under prep.
D4	Hubballi - Chikjajur	190	190	-	1850	CE/II/UBL & II/BNC	Commissioned on 27.03.2025
D5	Arsikere - Tumakuru	96	96	-	758	CE/II/BNC	Commissioned on 25.02.2022
D6	Birur - Shimoga	60	-	60	383	CE/II/BNC	Frozen by Rty Bd.
D7	Yelahanka - Penukonda	120	120	-	1255	CE/II/BNC	Commissioned on 28.03.2022
D8	Baiyappanahalli - Hosur	48	10	38	499	KRIDE	Jul-2025
D9	Yesvantpur - Channasandra	25	-	25	314	KRIDE	Aug-2025
D10	Bengaluru-Krishnarajapuram - Whitefield Quadrupling	38	-	38	493	GSU/SBC	Jun-2025
D11	Penukonda - Dharmavaram	42	-	42	308	CE/II/BNC	Jun-2025
D12	Hosapete-Hubballi-Londa- Vasco	312	261	51	3693	RVNL	Dec-2027
D13	Hosur-Omalur	147	-	147	1938	CE/II/BNC	DPR under process for sanction
D14	Ramanagaram-Mysore	94	94	-	1200	CE/II/BNC	Commissioned during 2017
D15	Hosadurga Road - Chikjajur	29	29	-	301	CE/II/BNC	Commissioned during 2015
D16	Chandorgaon-Cansaulim Rail Flyover	16	-	16	1892	CE/II/UBL	Survey under progress for ROR
D17	Bettahalsoor-Rajanukunte	6.14	-	6.14	248.24	CE/II/BNC	One year after LA
TOTAL		1716	1227	489	19330		
